



Abandoned Mine Lands

February 2022

AMLER Status Report

Program Overview

The Kentucky Division of Abandoned Mine Lands facilitates the distribution of federally funded AMLER Grants. These grants are geared toward economic and community development with correlations to historic, AML eligible, mine site.

January Events

- There were 28 Pilot Progress Meetings and 6 site visits.
- The vetting packages for HCTC Linemen Training Expansion (2017), KCWSD Generators (2019), Ashland Convention Center (2021), and Wolfpit Industrial Park (2021) were submitted to OSMRE for review.
- Mine histories were completed for Leeco Campground (2021), Manchester: Farm Here (2021), and Southeast Training Center (2021).
- The Memorandum of Agreement (MOA) was executed for EastPark Building for Project Jobs

Current Status and Date Since Last Movement

Vetting Package Development

Apple Cold Storage	11/12/2021
Highlands ARH Equipment	11/12/2021
Leeco Campground	11/12/2021
Manchester: Farm Here	11/23/2021
Sag Hollow	11/12/2021
Southeast Training Center	11/12/2021
Whitesburg Agritech	11/12/2021

OSMRE Vetting Review

HCTC Lineman Training Expansion	1/27/2022
Rush Off Road	8/21/2019
KCWSD Generators	1/6/2022
BPM Lumber Value-Add	4/8/2021
Ashland Convention Center	1/6/2022
Wolfpit Industrial Park	1/6/2022

MOA Development

Whitesburg Farmers Market Pavilion	9/30/2021
Kentucky Coal Heritage Trail	9/30/2021

NEPA Review

Federal Prison at Roxana Waterline	6/2/2021
Harlan County River Launches	9/2/2021
USA Drone Port	10/14/2020
Duval Valley Area	8/1/2020

OSMRE ATP Review

Beattyville Connect	12/17/2021
Impact Outdoors Phase III	11/2/2021
Drone Port Water and Sewer	11/4/2021
Mine Made Adventures	8/24/2021
Paintsville Sewer Expansion	12/22/2021
Wayland to Lackey Waterline Replacement	9/10/2021

Construction in Progress

Appalachian Wildlife Center	12/27/2016
HCTC Utility Training Program	11/1/2018
Portal 31 and Other Improvements	8/31/2021
Royalton Trail Town	3/25/2019
Historic Stearns	12/26/2019
Knott-Perry Route 80 & 476 Interconnect WSP	11/1/2020
Martin County Water Controls and Mods	9/1/2021
Outdoor Ventures Corporation Expansion Project	8/30/2021
PMC's Children's Hospital	7/17/2020

In anticipation of receiving 2022 AMLER Grant Funds, DAML has begun accepting applications. The 2022 application period is January 15th – April 1st.





EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

AMLER Program Review

Grant Year	Total Projects	Grant Funding	Expended	% Spent
2016	9	\$ 30,000,000.00	\$ 20,970,709.12	70%
2017	13	\$ 25,000,000.00	\$ 14,882,327.82	60%
2018	12	\$ 25,000,000.00	\$ 8,821,470.48	35%
2019	12	\$ 25,000,000.00	\$ 4,757,414.03	19%
2020	9	\$ 25,000,000.00	\$ 25,402.35	0%
2021	9	\$ 10,000,000.00	\$ -	0%
TOTAL	64	\$ 140,000,000.00	\$ 49,457,323.80	35%

Grant	Grant	Development Phase	Active	Complete
2016	9	0	4	5
2017	13	5	3	5
2018	12	8	1	3
2019	12	9	2	0
2020	9	8	1	0
2021	9	9	0	0
Total	64	39	11	13

Total Counties With AMLER Projects 21

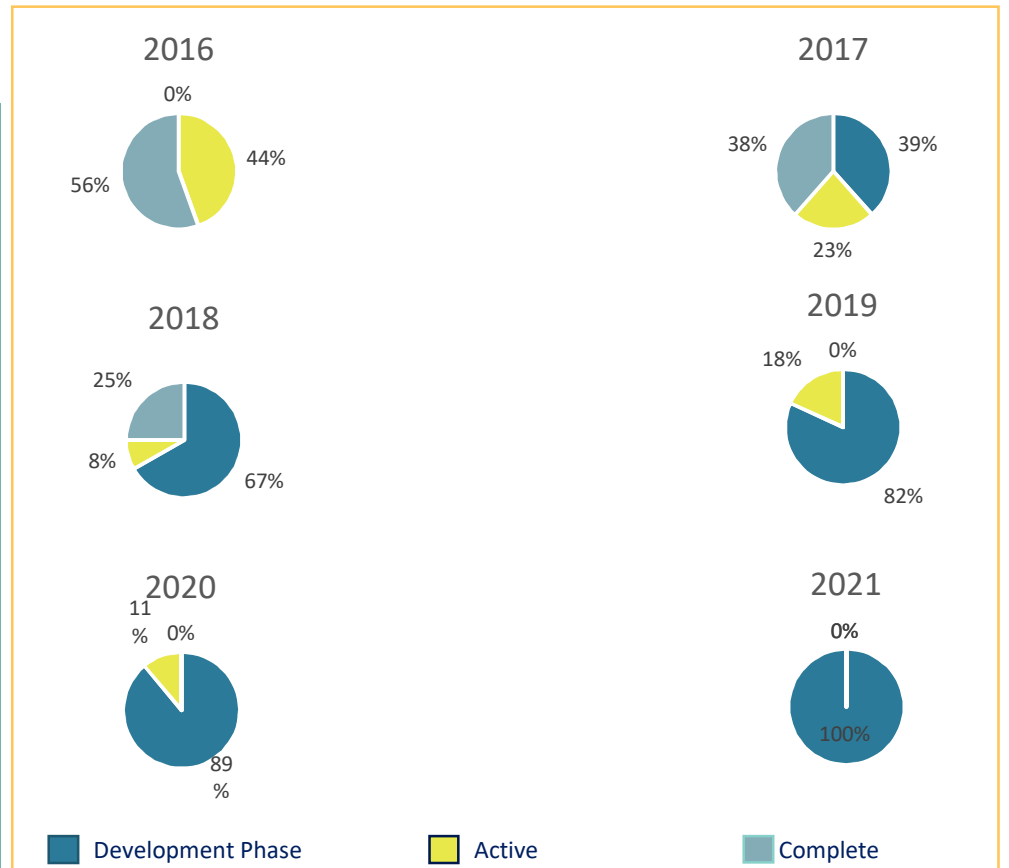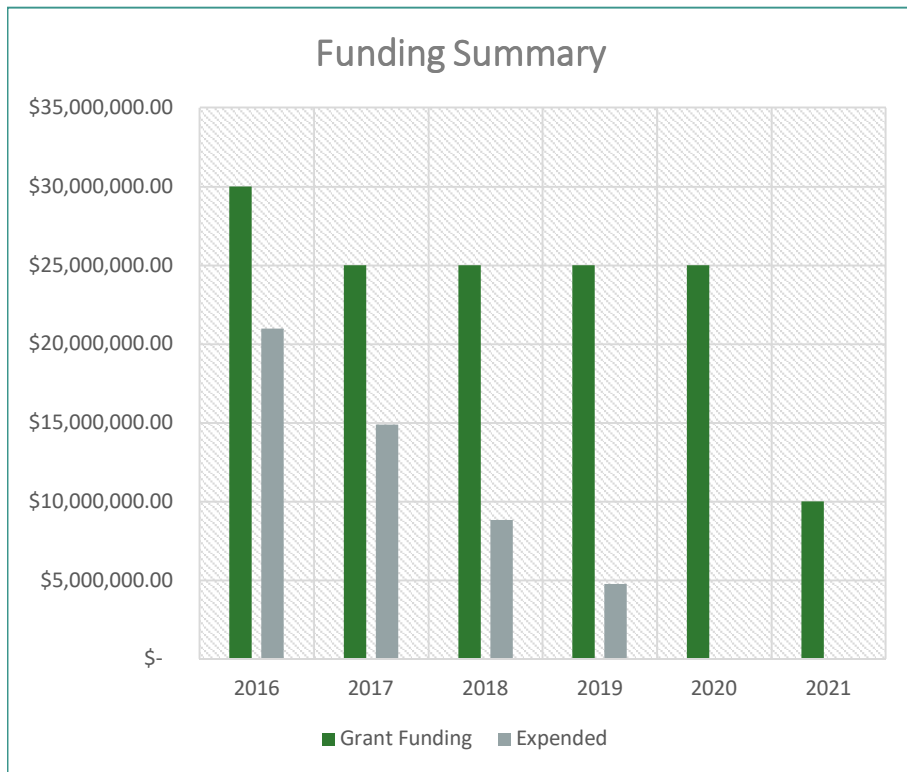



Abandoned Mine Lands


February 2022

2016




EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS


2016 Year Review



Total Projects	9
Total Active	4
Total in Development	0
Total Complete	5

Grant Totals	
Funding	\$30,000,000.00
Expended	\$20,970,709.12
Remaining	\$9,029,290.88
% Spent	69.90%

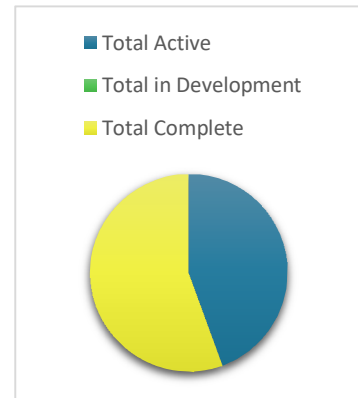

<div><div>Total Active</div><div>Total in Development</div><div>Total Complete</div></div> <div></div>	Totals																					
	9	9	9	9	9	9	9	9	9	9	9	9	9	9	9	9	9	9	9	5	5	
	Application Submitted	Application Review / Accepted	Mine History Conducted	Selection Team Review	Selection	Notification of Selection	Vetting Package Developed	Submission to OSMRE for Vetting	Vetting Approval	Press Release	Introductory Meeting	MOA Executed	Designer / Engineer Selected	Formal Plans to AML	NEPA Review	ATP Submission	Most Recent ATP Approval	Project Implementation After Design	Grantee Project Inspection	AML Project Inspection	Project Completion	Completion report
Appalachian Wildlife Center																						
eKAMI Phase I																						
HCTC Utility Training Program																						
Impact Outdoor Adventures																						
Marion Branch Industrial Development																						
Portal 31 and Other Improvements																						
Prestonsburg to David Rails to Trails																						
Royalton Trail Town																						
South Fork Elk View Waterline & Campground																						

Under Revision

Completed



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2016 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Appalachian Wildlife Center	Bell	\$12,500,000.00	\$6,940,991.16	55.53%	Progress Meeting held on 1-13-2022. Site visit made on 1-12-2022. Building construction continues. The base foundation, basement, structural steel and concrete floors are complete. Work continues on the exterior walls. The parking lots have been paved with base coat. The water tank, water lines and pump stations are complete. Electric service has been run to the site. Issues with an acceptable waste water site has AWC looking into a treatment and re-use facility for irrigation of wildlife plots. AWC is working on a proposal to re-allocate AMLER funds toward more current projects.
eKAMI Phase I	Johnson	\$2,500,000.00	\$2,500,000.00	100.00%	Project is complete.
HCTC Utility Training Program	Leslie	\$1,150,000.00	\$1,142,590.20	99.36%	Email update was received on 1-28-22. Program continues to produce CDL drivers. Grantee is spending the balance of the grant funds on salaries and program supplies. Awaiting final invoice.
Impact Outdoor Adventures	Clay	\$500,000.00	\$500,000.00	100.00%	Project is complete
Marion Branch Industrial Development	Pike	\$5,000,000.00	\$5,000,000.00	100.00%	Project is complete. DAML was notified Appalachian Tank, Inc., a subsidiary of Plantinum Tank Group, will be occupying the building. They anticipate to bring at least 50 jobs to the region.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2016 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Portal 31 and Other Improvements	Harlan	\$2,550,000.00	\$188,820.00	7.40%	Phase I of Portal 31 is set to begin in January by Jennmar. Phase II (the animatronics) has been bid. CED will complete Phase II pending an AVS check. The Bathhouse and High Tower engineering contracts are in negotiations with architect, Gibson Taylor Thompson. The High Point Tower plans need to be modified to meet KY Nature Preserves conditions.
Prestonsburg to David Rails to Trails	Floyd	\$1,950,000.00	\$1,949,620.44	99.98%	Project is complete.
Royalton Trail Town	Magoffin	\$1,900,000.00	\$798,687.32	42.04%	Progress meeting held on 1/25/2022. Summit has been selected to provide inspection services for the utilities phase of the contract, however that phase is currently in question due to discrepancies in the plans and bid advertisement. It is possible that this contract will need to be re-advertised and re-bid.
South Fork Elk View Waterline & Campground	Breathitt	\$1,950,000.00	\$1,950,000.00	100.00%	Project is complete.



Abandoned Mine Lands

February 2022

2017



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2017 Year Review

Remaining,
\$10,117,672.18



Expended,
\$14,882,327.82

Total Projects	13
Total Active	3
Total in Development	5
Total Complete	5

Grant Totals	
Funding	\$25,000,000.00
Expended	\$14,882,327.82
Remaining	\$10,117,672.18
% Spent	59.53%

■ Total Active
■ Total in Development
■ Total Complete



	Totals																					
	13	13	13	13	13	13	13	13	11	12	12	11	11	9	8	8	8	8	8	8	5	5
	Application Submitted	Application Review / Accepted	Mine History Conducted	Selection Team Review	Selection	Notification of Selection	Vetting Package Developed	Submission to OSMRE for Vetting	Vetting Approval	Press Release	Introductory Meeting	MOA Executed	Designer / Engineer Selected	Formal Plans to AML	NEPA Review	ATP Submission	Most Recent ATP Approval	Project Implementation After Design	Grantee Project Inspection	AML Project Inspection	Project Completion	Completion report
Coalfields Regional Industrial Park Gas Supply																						
EastPark Industrial Park Infrastructure and Development																						
eKAMI Phase II																						
Federal Prison at Roxana Waste Water Treatment Plant																						
Federal Prison at Roxana Waterline Extensions																						
HCTC Lineman Training Expansion																						
Historic Stearns																						
Impact Outdoors Phase II																						
KEIP Spec Building																						
Knott-Perry Route 80 & 476 Interconnect WSP																						
Martin County Water Controls and Mods																						
Rush Off Road																						
Whitesburg Farmers Market Pavilion																						
Unassigned Funds																						

Under Revision

Completed



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2017 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Coalfields Regional Industrial Park Gas Supply	Perry	\$900,000.00	\$900,000.00	100.00%	Project is complete.
EastPark Industrial Park Infrastructure and Development	Boyd	\$4,000,000.00	\$3,999,967.00	100.00%	Project is complete.
eKAMI Phase II	Johnson	\$1,000,000.00	\$1,000,000.00	100.00%	Project is complete.
Federal Prison at Roxana Waste Water Treatment Plant	Letcher	\$182,635.00	\$182,635.00	100.00%	The OSMRE Lexington Field Office was advised that this grant would be tabled on 04-12-2021. Originally allotted \$500,000 in grant funds. April 2021, remaining funds were reallocated. Any engineering/plans will be retained for potential future development. \$300,000 will be reassigned to Whitesburg Farmers Market with \$17,365.00 to Unassigned Funds.
Federal Prison at Roxana Waterline Extensions	Letcher	\$3,800,000.00	\$255,864.50	6.73%	Progress meeting held on 1-26-2022. Design plans were received by AML on 6-01-2021. Elements of the project that relate to the Federal Prison project will be left off the contract and the waterline extension project will be bid and constructed. AML received Cost Estimate from Bell Engineering on 7-08-2021 and the NEPA process began. KY Heritage Council requested an Archeological Review. The Archeological Review has been developed and submitted to the KY Heritage Council.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2017 Project Status

	County	Grant Funding	Expended	% Expended	Comments
HCTC Lineman Training Expansion	Perry	\$280,000.00	\$-	0.00%	Grantee was selected to receive \$280,000 of funding remaining from the 2017 Grant Year. Grantee was notified on 11-16-2021. A revised application was requested from the grantee. Revised application was received on 1-10-2022. Vetting package sent to OSMRE on 1-27-2022.
Historic Stearns	McCreary	\$1,100,000.00	\$408,078.60	37.10%	Work on the engine and passenger cars has finished. The Blue Heron Trestle Bridge Pedestrian Walkway has been dropped from the scope of work. Queen City is obtaining materials to complete the track installation.
Impact Outdoors Phase II	Clay	\$200,000.00	\$199,711.42	99.86%	Project is complete
KEIP Spec Building	Pike	\$5,720,000.00	\$5,643,282.31	98.66%	Project is complete.
Knott-Perry Route 80 & 476 Interconnect WSP	Knott	\$1,250,000.00	\$1,080,531.88	86.44%	A progress meeting was held on 1-11-2022. Currently awaiting delivery of back-up generators for pump stations. MOA is being extended due to the delay.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2017 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Martin County Water Controls and Mods	Martin	\$2,250,000.00	\$1,212,257.11	53.88%	Construction Progress Meeting held on 1-19-2022. Work continues to take place at Water Treatment Plant and Raw Water Intake locations. The concrete vault has been poured at the RWI location and ramp installation is complete. Concrete piles have been poured as well. All contents of Clarifier #1 have been removed to prepare for reconditioning. Project continues on schedule.
Rush Off Road	Boyd	\$4,000,000.00	\$-	0.00%	AML is working with OSMRE to approve the site location change.
Whitesburg Farmers Market Pavilion	Letcher	\$300,000.00	\$-	0.00%	Progress Meeting was held 1-11-2022. Project was selected for vetting in April 2021 after funding was reallocated from Federal Prison at Roxana Waste Water Treatment Plant. Vetting Package sent to OSMRE on 06-24-2021. Vetting approval was received on 9-30-2021. MOA is being developed.
Unassigned Funds	0	\$17,365.00	\$-	0.00%	Balance remaining unassigned after reallocation of the Federal Prison at Roxana Waste Water Treatment Plant funds.



Abandoned Mine Lands


February 2022

2018




EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2018 Year Review



Total Projects	12
Total Active	1
Total in Development	8
Total Complete	3

Grant Totals	
Funding	\$25,000,000.00
Expended	\$8,821,470.48
Remaining	\$16,178,529.52
% Spent	35.29%

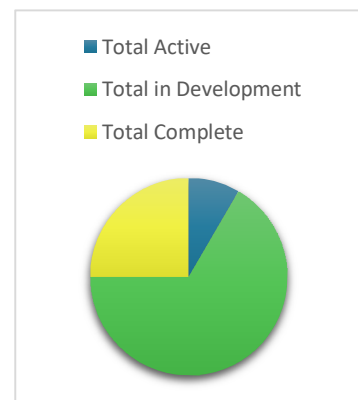

	Totals																					
	12	12	12	12	12	12	12	12	12	12	11	10	8	6	6	4	4	4	4	3	3	
	Application Submitted	Application Review / Accepted	Mine History Conducted	Selection Team Review	Selection	Notification of Selection	Vetting Package Developed	Submission to OSMRE for Vetting	Vetting Approval	Press Release	Introductory Meeting	MOA Executed	Designer / Engineer Selected	Formal Plans to AML	NEPA Review	ATP Submission	Most Recent ATP Approval	Project Implementation After Design	Grantee Project Inspection	AML Project Inspection	Project Completion	Completion report
Beattyville Connect																						
BSFSR Blue Heron Spur Slide (Rail Steel Installation)																						
eKAMI Prison Reform																						
Harlan County River Launches																						
Historic Stearns (Blue Heron Slide Repair)																						
Impact Outdoors Phase III																						
Kentucky Coal Heritage Trail																						
Martin Water System Improvements - Big Sandy																						
Outdoor Ventures Corporation Expansion Project																						
Project Core (Dajcor)																						
Thunder Mountain																						
USA Drone Port																						

Total Active

Total in Development

Total Complete

Under Revision

Completed



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2018 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Beattyville Connect	Lee	\$1,250,000.00	\$129,688.00	10.38%	Progress Meeting held on 1-25-2022. Submitted to OSM for ATP approval on 12-17-2021.
BSFSR Blue Heron Spur Slide (Rail Steel Installation)	McCreary	\$334,000.00	\$255,335.20	76.45%	Project is complete.
eKAMI Prison Reform	Morgan	\$6,400,000.00	\$169,832.13	2.65%	There has been no change in the status. MOA is under development for the modified eKAMI Prison Reform/Workforce Development grant. The design has been on hold during vetting and will revisit the current plans.
Harlan County River Launches	Harlan	\$376,000.00	\$15,000.00	3.99%	Progress Meeting 1-06-2022. Plans from SynTerra were submitted 09-02-2021 and AML has begun the process of developing the NEPA.
Historic Stearns (Blue Heron Slide Repair)	McCreary	\$1,500,000.00	\$1,338,886.90	89.26%	Project is complete.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2018 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Impact Outdoors Phase III	Clay	\$350,000.00	\$-	0.00%	Progress Meeting held on 1-27-2022. MOA has been executed. Design plans are complete. Request for ATP sent to OSMRE on 11-02-2021.
Kentucky Coal Heritage Trail	Floyd	\$225,000.00	\$-	0.00%	Progress Meeting held on 1-04-2022. MOA is being developed. Grantee will consider RFQ while MOA is being fully executed.
Martin Water System Improvements - Big Sandy	Martin	\$2,000,000.00	\$100,494.73	5.02%	Bell Engineering and Martin Co. Water District have requested that this project be put on hold as they assess the need for certain elements of this project. All elements may not be required in order to reach the goal of pumping water to the Big Sandy Penitentiary.
Outdoor Ventures Corporation Expansion Project	McCreary	\$3,500,000.00	\$265,750.22	7.59%	MOA has been fully executed. OVC is in the process of purchasing equipment and machinery.
Project Core (Dajcor)	Perry	\$6,500,000.00	\$6,492,640.00	99.89%	Project is Complete



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2018 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Thunder Mountain	Letcher	\$1,065,000.00	\$-	0.00%	Grantee had to select an alternate site. On 4-27-2021, the grantee provided details of the new site and a request for approval of the site change to AML. On 5-08-2021, AML responded that the proposed locations are on or near a currently bonded permit and asked grantee for clarification. On 8-05-2021, grantee had a meeting with DMRE and DMP to work through permitting issues on and adjacent to the site. Site visit conducted 11-23-2021. Engineering selection interviews held on 1-26-2022.
USA Drone Port	Knott	\$1,500,000.00	\$53,843.30	3.59%	Progress Meeting was held on 1-03-2022. Grantee gave an update on issues with site access. Initial site is no longer viable. Drone Port Borad to meet 1-20-2022 to discuss alternate locations. Will submit to AML at the next meeting. MOA extended.



Abandoned Mine Lands


February 2022

2019




EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2019 Year Review



Total Projects	12
Total Active	2
Total in Development	9
Total Complete	0

Grant Totals	
Funding	\$25,000,000.00
Expended	\$4,757,414.03
Remaining	\$20,242,585.97
% Spent	19.03%

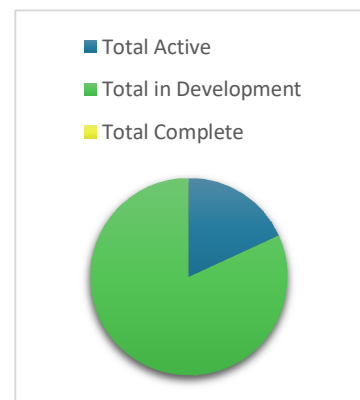

	Totals																					
	11	11	11	11	11	11	12	12	11	11	11	11	9	6	6	6	2	2	1	1	0	0
	Application Submitted	Application Review / Accepted	Mine History Conducted	Selection Team Review	Selection	Notification of Selection	Vetting Package Developed	Submission to OSMRE for Vetting	Vetting Approval	Press Release	Introductory Meeting	MOA Executed	Designer / Engineer Selected	Formal Plans to AML	NEPA Review	ATP Submission	Most Recent ATP Approval	Project Implementation After Design	Grantee Project Inspection	AML Project Inspection	Project Completion	Completion report
Advanced Manufacturing and Construction Center																						
Drone Port Water and Sewer																						
International Landing Zone																						
KCWSD Generators																						
Leslie County Connectivity & Teleworks																						
Mine Made Adventures																						
Paintsville Sewer Expansion																						
Pinnacle Park																						
PMC's Children's Hospital																						
South Fork Elk View Phase II																						
Thunder Mountain Phase II																						
Wayland to Lackey Waterline Replacement																						

Under Revision

Completed



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2019 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Advanced Manufacturing and Construction Center	Perry	\$2,500,000.00	\$-	0.00%	Progress Meeing was held on 1-05-2022. Phase I design is complete and is under review by HCTC. Once approved, will be sent to AML for review and NEPA.
Drone Port Water and Sewer	Knott	\$743,000.00	\$85,665.00	11.53%	Progress meeting held 1-22-2022. AML's environmental assessment has been completed. A formal ATP request has been assembled and submitted to OSMRE.
International Landing Zone	Martin	\$1,370,000.00	\$-	0.00%	Progress Meeting held on 1-20-2022. GRW has been selected as the engineering firm and contract documents are being finalized.
KCWSD Generators	Knott	\$600,000.00	\$-	0.00%	Project was selected for vetting on 11-16-2021. Will be funded with funds remaining from 2019 Grant Year. Vetting documents were sent to OSMRE on 1-06-2022.
Leslie County Connectivity & Teleworks	Leslie	\$2,056,000.00	\$-	0.00%	Progress Meeting held on 1-04-2022. MOA has been fully executed. Leslie County Fiscal Court if finalizing agreements with property owners at the tower sites.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2019 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Mine Made Adventures	Knott	\$1,706,000.00	\$140,304.77	8.22%	There has been no change in the status. An eligibility determination has been requested to OLS on 5-13-2021 and again on 1-07-2022. Request for ATP was sent to OSMRE on 8-24-2021.
Paintsville Sewer Expansion	Johnson	\$4,000,000.00	\$371,730.93	9.29%	An ATP request was sent to OSM on 12-22-2021. A progress meeting was held on 1-25-2022. Grantee continues to make progress on meeting the requirements of the other two funding sources. Bocook Engineering continues to secure the required easements.
Pinnacle Park	Martin	\$2,000,000.00	\$-	0.00%	Progress Meeting held on 1-22-2022. Summit Engineering has been selected as the engineer and contract documents are being finalized.
PMC's Children's Hospital	Pike	\$4,780,000.00	\$3,974,204.94	83.14%	A progress meeting was held on 12-09-2021. Construction is complete. Ribbon cutting ceremony was held 12-2-2021. Awaiting final invoice and project summary from PMC.
South Fork Elk View Phase II	Breathitt	\$1,345,000.00	\$67,444.75	5.01%	Progress meeting held 1-27-2022. USDA Rural Development has accepted AML's environmental review. The FONSI has been posted to the local newspaper. The Engineer is preparing bidding documents. AML is waiting on USDA RD's final approval before the project can move forward.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2019 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Thunder Mountain Phase II	Letcher	\$2,400,000.00	\$-	0.00%	Grantee had to select an alternate site. On 4-27-2021, the grantee provided details of the new site and a request for approval of the site change to AML. On 5-08-2021, AML responded that the proposed locations are on or near a currently bonded permit and asked grantee for clarification. On 8-05-2021, grantee had a meeting with DMRE and DMP to work through permitting issues on and adjacent to the site. Site visit conducted 11-23-2021. Engineering selection interviews held on 1-26-2022.
Wayland to Lackey Waterline Replacement	Floyd	\$1,500,000.00	\$118,063.64	7.87%	Progress meeting held on 1-20-2022. Request for ATP submitted to OSMRE on 9-10-2021. Waiting on ATP approval from OSMRE.



Abandoned Mine Lands


February 2022

2020




EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2020 Year Review



Total Projects	9
Total Active	1
Total in Development	8
Total Complete	0

Grant Totals	
Funding	\$25,000,000.00
Expended	\$25,402.35
Remaining	\$24,974,597.65
% Spent	0.10%

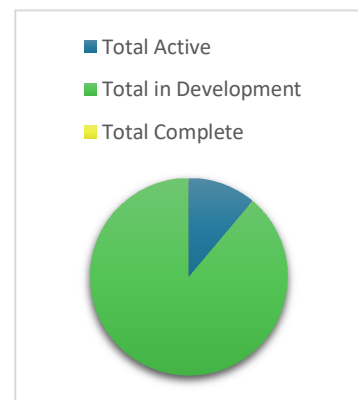

	Totals																					
	9	9	9	9	9	9	9	9	8	9	8	8	5	2	1	1	1	0	0	0	0	0
	Application Submitted	Application Review / Accepted	Mine History Conducted	Selection Team Review	Selection	Notification of Selection	Vetting Package Developed	Submission to OSMRE for Vetting	Vetting Approval	Press Release	Introductory Meeting	MOA Executed	Designer / Engineer Selected	Formal Plans to AML	NEPA Review	ATP Submission	Most Recent ATP Approval	Project Implementation After Design	Grantee Project Inspection	AML Project Inspection	Project Completion	Completion report
Buckhorn WTP & 15-7 Interconnect																						
BPM Lumber Value-Add																						
EastPark Building for Project Jobs																						
Duval Valley Area																						
Harlan County Business Park Gas Infrastructure																						
King's Daughters Health System Expansion																						
Lynch Motorsports Welcome Center																						
PMC Cancer Center Expansion																						
Wheelwright Water System																						
AML Administrative Costs																						

Under Revision

Completed



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2020 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Buckhorn WTP & 15/7 Interconnect	Perry	\$3,500,000.00	\$25,402.35	0.73%	Progress meeting held on 1-18-2022. MOA has been executed. Design process underway for Buckhorn Water Treatment Plant. The 15/7 Interconnect portion is in the initial design process. Engineer will soon file for CSX permit for that project.
BPM Lumber Value-Add	Laurel	\$3,769,000.00	\$-	0.00%	A revised application was submitted by the grantee and submitted to OSMRE on 8-27-2021. Project is in the OSMRE Vetting process. OSMRE asked questions concerning Real Property on 10-08-2021 and AML sent responses from the grantee on 10-27-2021.
EastPark Building for Project Jobs	Boyd	\$1,500,000.00	\$-	0.00%	The MOA has been fully executed. The grantee is working with client about moving forward.
Duvall Valley Area	Clinton	\$3,000,000.00	\$-	0.00%	Progress meeting held on 12-21-21. Response to KHC questions sent on 01/10/22. Awaiting reply from KY Heritage Council.
Harlan County Business Park Gas Infrastructure	Harlan	\$1,500,000.00	\$-	0.00%	Progress meeting was held on 12-09-2021. MOA in EEC Legal review. Engineering Selection held 11-22-2021. HDR selected as engineering firm pending final approval from Harlan Co Fiscal Court.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2020 Project Status

	County	Grant Funding	Expended	% Expended	Comments
King's Daughters Health System Expansion	Boyd	\$4,000,000.00	\$-	0.00%	KDMC is advertising and purchasing equipment.
Lynch Motorsports Welcome Center	Harlan	\$400,000.00	\$-	0.00%	Progress Meeting was held on 1-06-2022. MOA executed on 10-12-2021. RFQ has been advertised, submissions are under review.
PMC Cancer Center Expansion	Pike	\$4,270,000.00	\$-	0.00%	Progress meeting held on 1-13-2022. MOA was executed on 10-29-2021. Contract for TEG Architect approved by AML.
Wheelwright Water System	Floyd	\$2,050,000.00	\$-	0.00%	Progress meeting held on 1-19-2022. Maxim Engineering has begun the design process.
AML Administrative Costs	0	\$1,011,000.00	\$-	0.00%	



Abandoned Mine Lands


February 2022

2021



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2021 Year Review



Total Projects	9
Total Active	0
Total in Development	9
Total Complete	0

Grant Totals	
Funding	\$10,000,000.00
Expended	\$-
Remaining	\$10,000,000.00
% Spent	0.00%

	Totals																						
	9	9	9	9	9	9	3	2	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
	Application Submitted	Application Review / Accepted	Mine History Conducted	Selection Team Review	Selection	Notification of Selection	Vetting Package Developed	Submission to OSMRE for Vetting	Vetting Approval	Press Release	Introductory Meeting	MOA Executed	Designer / Engineer Selected	Formal Plans to AML	NEPA Review	ATP Submission	Most Recent ATP Approval	Project Implementation After Design	Grantee Project Inspection	AML Project Inspection	Project Completion	Completion report	
Apple Cold Storage																							
Ashland Convention Center																							
Highlands ARH Equipment																							
Leeco Campground																							
Manchester: Farm Here																							
Sag Hollow																							
Southeast Training Center																							
Whitesburg Agritech																							
Wolfpit Industrial Park																							
AML Administrative Costs																							

Under Revision

Completed



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2021 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Apple Cold Storage	Martin	\$2,500,000.00	\$-	0.00%	Vetting Package is being prepared.
Ashland Convention Center	Boyd	\$1,000,000.00	\$-	0.00%	Vetting package has been prepared and sent to OSMRE on 1-06-2022. The grantee is answering questions from OSMRE.
Highlands ARH Equipment	Floyd	\$750,000.00	\$-	0.00%	Vetting Package is being prepared.
Leeco Campground	Leslie	\$1,000,000.00	\$-	0.00%	Vetting Package is being prepared.
Manchester: Farm Here	Clay	\$700,000.00	\$-	0.00%	Vetting Package is being prepared.



EEC-DNR-ABANDONED MINE LANDS AMLER GRANTS

2021 Project Status

	County	Grant Funding	Expended	% Expended	Comments
Sag Hollow	Owsley	\$600,000.00	\$-	0.00%	Vetting Package is being prepared.
Southeast Training Center	Knox	\$750,000.00	\$-	0.00%	Vetting Package is being prepared.
Whitesburg Agritech	Letcher	\$1,000,000.00	\$-	0.00%	Vetting Package is being prepared.
Wolfpit Industrial Park	Pike	\$700,000.00	\$-	0.00%	Vetting Package submitted to OSMRE 1-06-2022
AML Administrative Costs	0	\$1,000,000.00	\$-	0.00%	
